



# Harris Phase 1 Exterior

Name	Assigned to	Start	Finish	% Complete	Oct 23	Oct 30	Nov 6	Nov 13	Nov 20
1 Mobilize		11/1/2022	11/2/2022	0					
2 Demolition		11/2/2022	11/23/2022	0					
3 Excavation		11/24/2022	12/26/2022	0					
4 MEP Groundwork		12/27/2022	1/2/2023	0					
5 Foundation/Footings		12/27/2022	1/24/2023	0					
6 Backfill		1/3/2023	1/9/2023	0					
7 Concrete Slab		1/10/2023	1/18/2023	0					
8 Pavers/Planters		1/19/2023	3/1/2023	0					
9 Water Feature		1/23/2023	2/24/2023	0					
10 Trellis - Steel/Wood		3/1/2023	3/9/2023	0					
11 Trellis Glass		3/10/2023	3/20/2023	0					
12 Cabinets		3/21/2023	3/21/2023	0					
13 Firepit Burner		3/15/2023	3/17/2023	0					
14 Counter tops		4/4/2023	4/4/2023	0					
15 Appliance installation		4/5/2023	4/5/2023	0					
16 Landscaping		4/6/2023	5/10/2023	0					
17 Final clean up		5/11/2023	5/17/2023	0					

# Harris Phase 1 Exterior

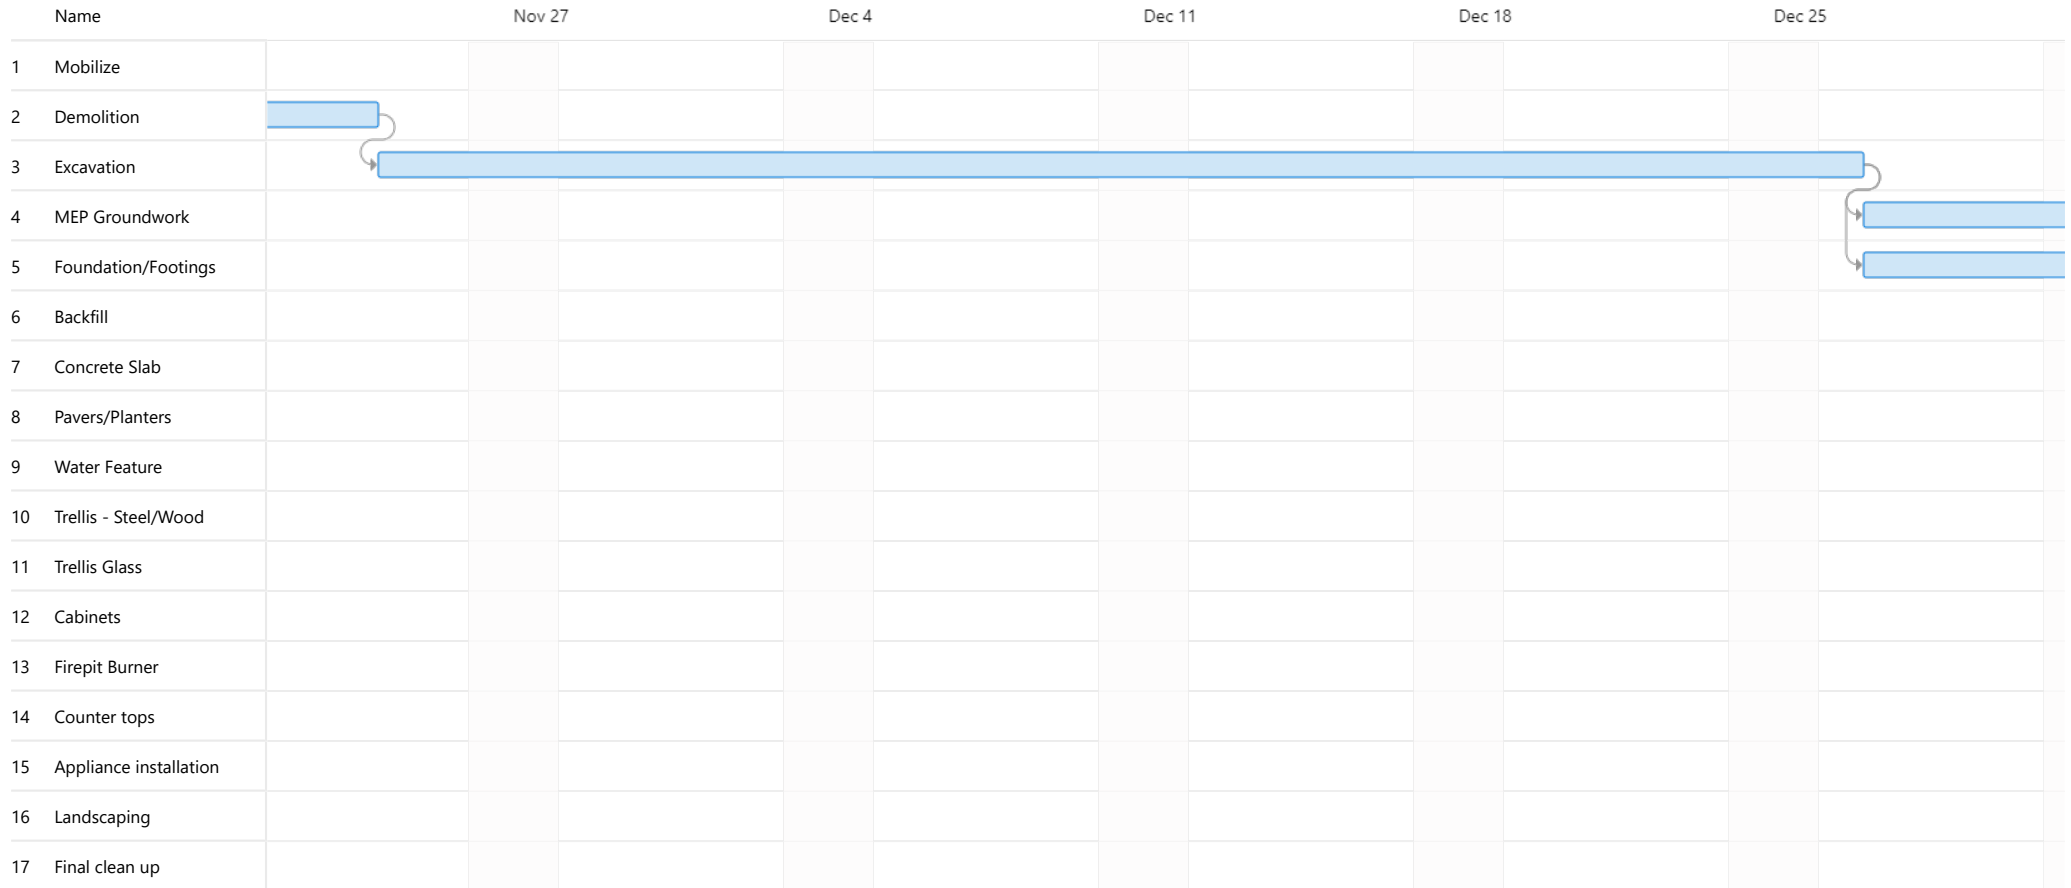

# Harris Phase 1 Exterior

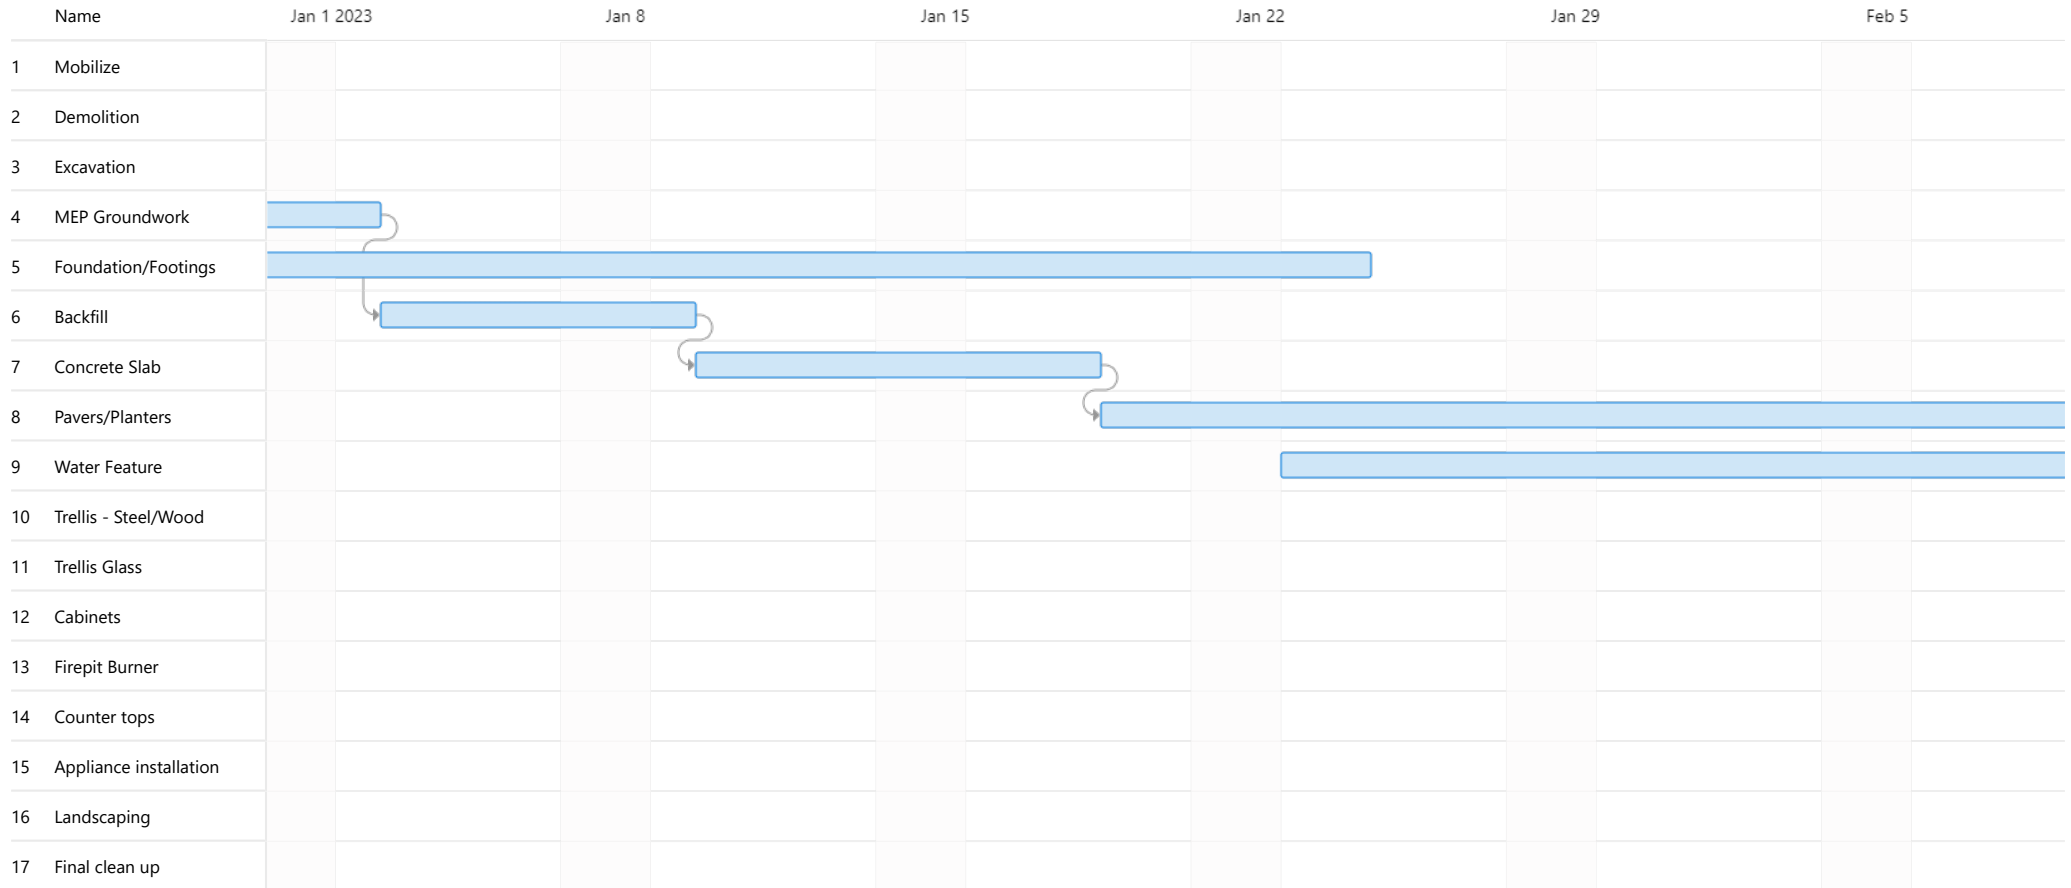


# Harris Phase 1 Exterior

Name	Feb 12	Feb 19	Feb 26	Mar 5	Mar 12	Mar 19
1 Mobilize						
2 Demolition						
3 Excavation						
4 MEP Groundwork						
5 Foundation/Footings						
6 Backfill						
7 Concrete Slab						
8 Pavers/Planters						
9 Water Feature						
10 Trellis - Steel/Wood						
11 Trellis Glass						
12 Cabinets						
13 Firepit Burner						
14 Counter tops						
15 Appliance installation						
16 Landscaping						
17 Final clean up						

# Harris Phase 1 Exterior

Name	Mar 26	Apr 2	Apr 9	Apr 16	Apr 23	Apr 30
1 Mobilize						
2 Demolition						
3 Excavation						
4 MEP Groundwork						
5 Foundation/Footings						
6 Backfill						
7 Concrete Slab						
8 Pavers/Planters						
9 Water Feature						
10 Trellis - Steel/Wood						
11 Trellis Glass						
12 Cabinets						
13 Firepit Burner						
14 Counter tops						
15 Appliance installation						
16 Landscaping						
17 Final clean up						



# Harris Phase 1 Exterior

Name	pr 30	May 7	May 14	May 21	May 28	Jun 4
1 Mobilize						
2 Demolition						
3 Excavation						
4 MEP Groundwork						
5 Foundation/Footings						
6 Backfill						
7 Concrete Slab						
8 Pavers/Planters						
9 Water Feature						
10 Trellis - Steel/Wood						
11 Trellis Glass						
12 Cabinets						
13 Firepit Burner						
14 Counter tops						
15 Appliance installation						
16 Landscaping						
17 Final clean up						
