




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	October					November				December				January			
							10/1	10/8	10/15	10/22	10/29	11/5	11/12	11/19	11/26	12/3	12/10	12/17	12/24	12/31	1/7	1/14	
1		Long Lead Items	175 days	Mon 11/27/23	Fri 8/2/24																		
2		Issue Permit	1 day	Mon 11/27/23	Mon 11/27/23																		
3		Receive Construction Drawings	10 days	Mon 11/27/23	Fri 12/8/23																		
4		Receive interior drawings	20 days	Tue 11/28/23	Tue 12/26/23	2																	
5		Submit and approve window package	10 days	Mon 12/11/23	Fri 12/22/23	3																	
6		Submit and approve roof package	10 days	Mon 12/11/23	Fri 12/22/23	3																	
7		Submit and approve cabinet package	20 days	Wed 12/27/23	Thu 1/25/24	4																	
8		Issue plumbing fixture package	20 days	Wed 12/27/23	Thu 1/25/24	4																	
9		Fabricate and deliver windows	85 days	Tue 12/26/23	Wed 4/24/24	5																	
10		Fabricate and deliver roofing	30 days	Tue 12/26/23	Wed 2/7/24	6																	
11		Fabricate and deliver cabinets	30 days	Fri 6/21/24	Fri 8/2/24	7																	
12		Fabricate and deliver plumbing fixture	20 days	Fri 1/26/24	Thu 2/22/24	8																	
13		Site Work	382 days?	Mon 11/27/23	Tue 5/27/25																		
14		Tree protection & TESC	1 day	Tue 11/28/23	Tue 11/28/23	2																	
15		Temp power set up & inspection	1 day	Wed 11/29/23	Wed 11/29/23	14																	
16		Utility locates	1 day	Wed 11/29/23	Wed 11/29/23	14																	
17		Demo existing hardscape	5 days	Tue 12/26/23	Tue 1/2/24	23																	
18		Utilities	5 days	Thu 11/30/23	Wed 12/6/23	16																	
19		Grading	5 days	Thu 1/2/25	Wed 1/8/25	42																	
20		Site Concrete	10 days	Thu 1/9/25	Thu 1/23/25	19																	
21		Landscape	20 days	Fri 1/24/25	Thu 2/20/25	20																	
22		Building Construction	382 days?	Mon 11/27/23	Tue 5/27/25																		
23		Demo house	17 days	Thu 11/30/23	Fri 12/22/23	16,2																	
24		Concrete footing prep & pour	15 days	Tue 12/26/23	Wed 1/17/24	23																	
25		Framing	55 days	Thu 1/18/24	Wed 4/3/24	24																	
26		Roofing	10 days	Thu 4/4/24	Wed 4/17/24	25																	
27		Window install	5 days	Thu 4/18/24	Wed 4/24/24	26																	
28		Plumbing rough-in	10 days	Thu 4/18/24	Wed 5/1/24	26																	
29		HVAC rough-in	10 days	Thu 5/2/24	Wed 5/15/24	28																	
30		Electrical rough-in	40 days	Thu 5/9/24	Fri 7/5/24	29FS-5 d																	
31		Low volt rough-in	40 days	Fri 6/7/24	Fri 8/2/24	30FS-20 d																	
32		Siding	10 days	Thu 4/25/24	Wed 5/8/24	27																	
33		Exterior paint	15 days	Thu 5/9/24	Thu 5/30/24	32																	
34		Insulation	10 days	Mon 8/5/24	Fri 8/16/24	31																	
35		Gutters and downspout install	2 days	Fri 5/31/24	Mon 6/3/24	33																	
36		Drywall	20 days	Mon 8/19/24	Mon 9/16/24	34																	
37		Tile install	40 days	Tue 9/17/24	Mon 11/11/24	36																	
38		Wood Flooring delivery & acclimatization	5 days	Tue 9/17/24	Mon 9/23/24	36																	
39		Wood Flooring install	10 days	Tue 10/1/24	Mon 10/14/24	38FS+5 d																	
40		Millwork install	20 days	Tue 10/15/24	Mon 11/11/24	39																	
41		Cabinet install	15 days	Tue 10/15/24	Mon 11/4/24	39																	
42		Interior paint	40 days	Tue 11/5/24	Tue 12/31/24	41																	
43		Countertop template & Fab	10 days	Tue 11/5/24	Mon 11/18/24	41																	
44		Countertop install	3 days	Tue 11/5/24	Thu 11/7/24	41																	

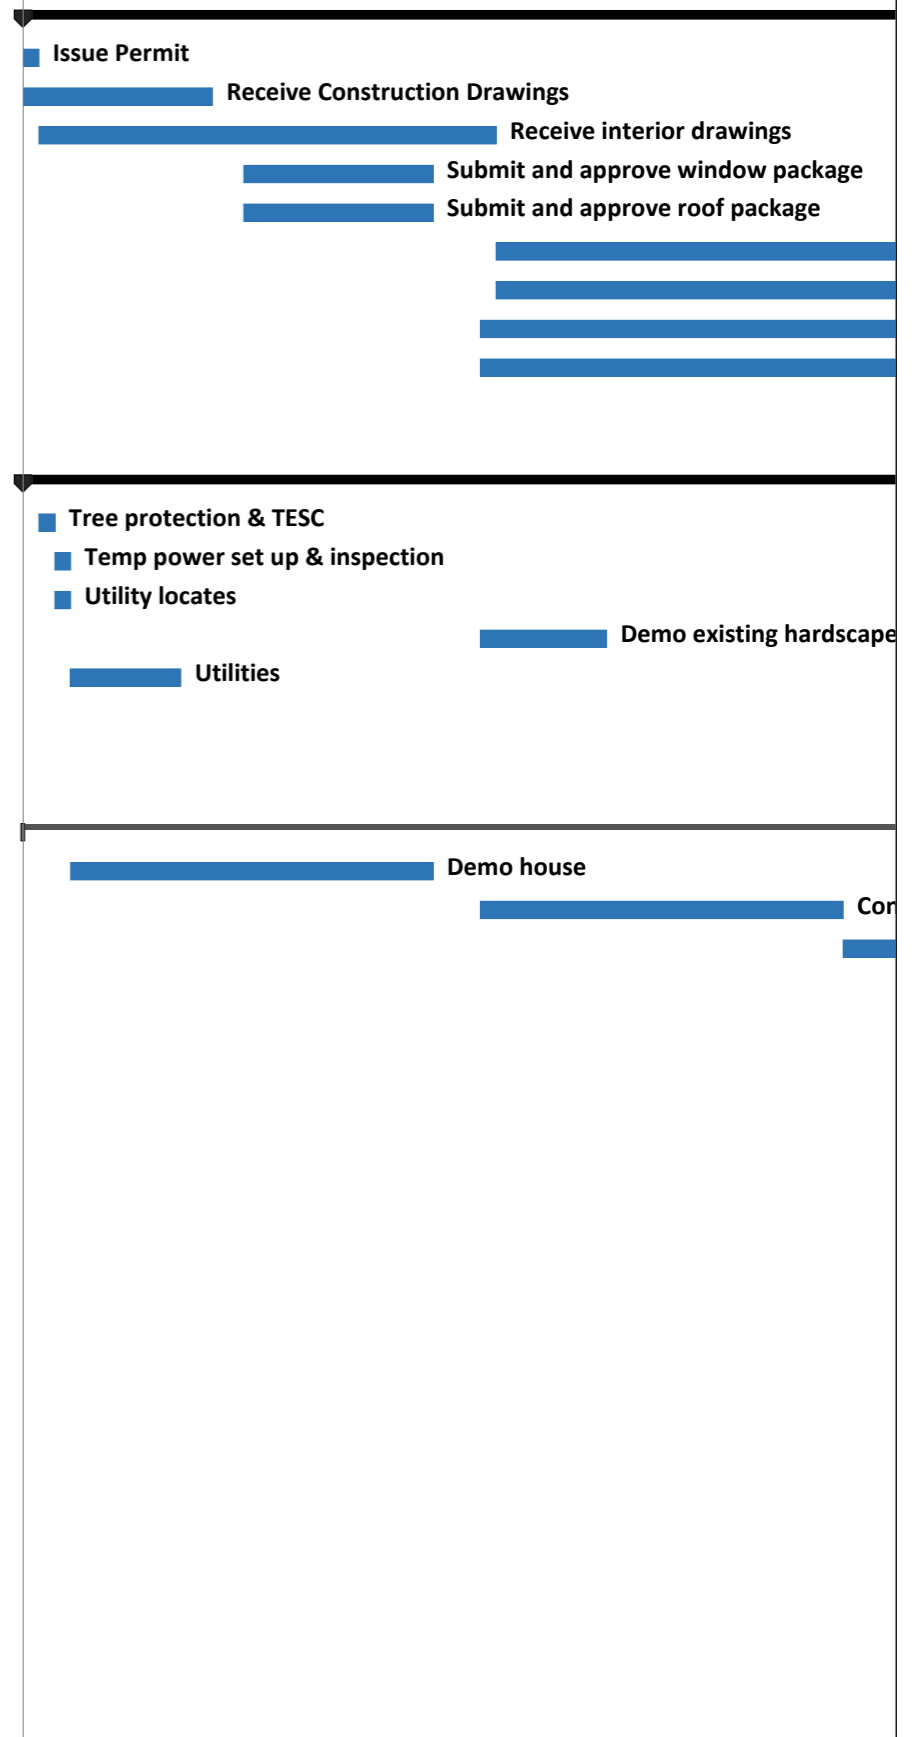


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	October				November				December				January			
							10/1	10/8	10/15	10/22	10/29	11/5	11/12	11/19	11/26	12/3	12/10	12/17	12/24	12/31	1/7	1/14
45		Electrical trim	20 days	Thu 1/2/25	Thu 1/30/25	42																
46		HVAC trim	20 days	Fri 1/31/25	Thu 2/27/25	45																
47		Plumbing trim	15 days	Fri 2/28/25	Thu 3/20/25	46																
48		Low volt trim	15 days	Fri 3/21/25	Thu 4/10/25	47																
49		Final clean	4 days	Fri 4/11/25	Wed 4/16/25	48																
50		Window cleaning	4 days	Thu 4/17/25	Tue 4/22/25	49																
51		Site final	1 day	Fri 4/11/25	Fri 4/11/25	48																
52		Final	1 day	Mon 4/14/25	Mon 4/14/25	51																
53		Punch list	30 days	Tue 4/15/25	Tue 5/27/25	52																
54			1 day?	Mon 11/27/2	Mon 11/27/2																	



pe

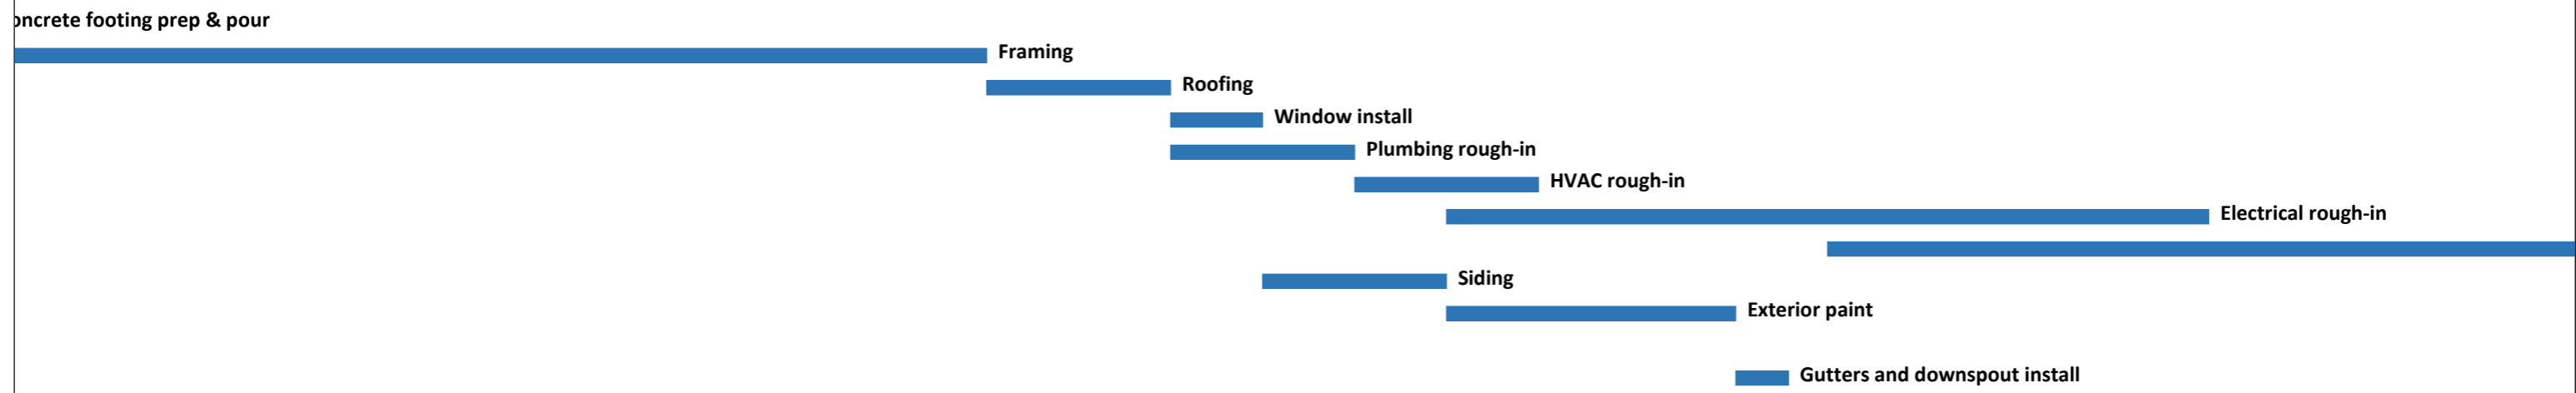

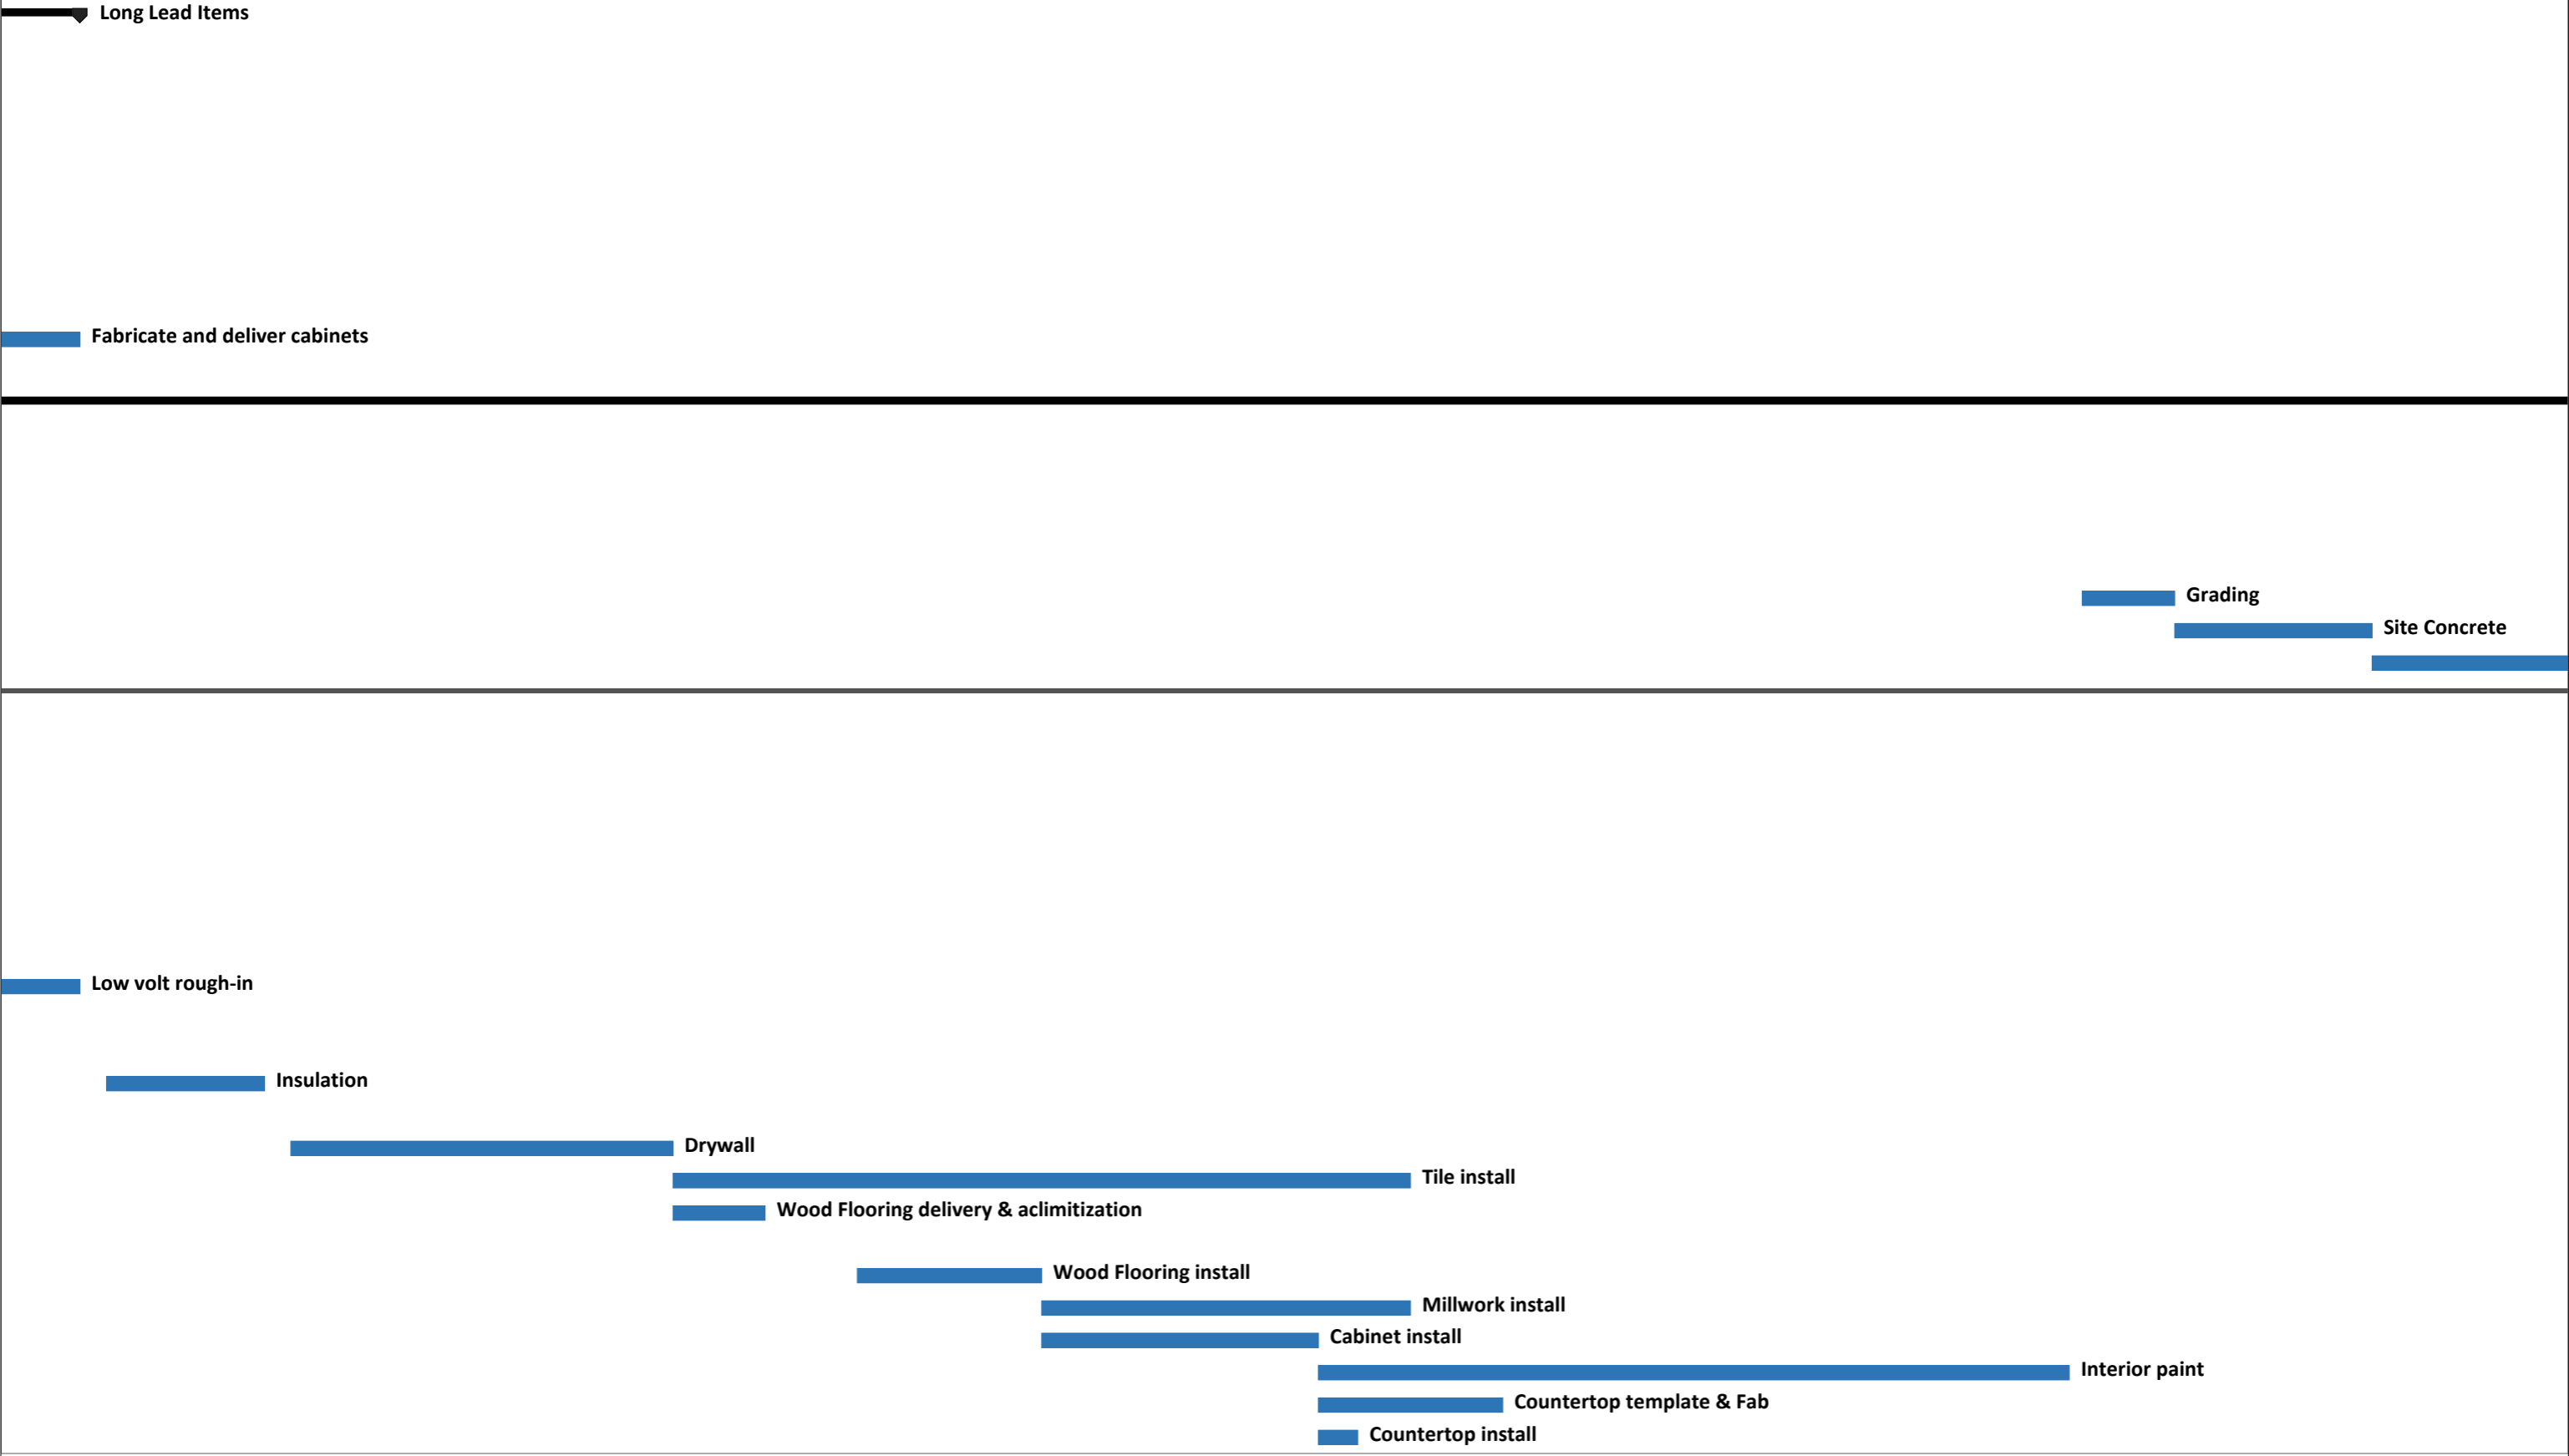

August					September				October				November				December				January				February		
7/28	8/4	8/11	8/18	8/25	9/1	9/8	9/15	9/22	9/29	10/6	10/13	10/20	10/27	11/3	11/10	11/17	11/24	12/1	12/8	12/15	12/22	12/29	1/5	1/12	1/19	1/26	2/2

Electrical
