


NO.	DESCRIPTION	DATE
7	SOIL STABILIZATION	05.02.24

CONSTRUCTION MONITORING NOTES

MONITOR ADJACENT BLDG. FOR SETTLEMENT. START MONITORING PRIOR TO DEMOLITION WEEKLY UNTIL PILE DRIVING IS COMPLETE. LEVELS TO BE MEASURED BY PROJECT SURVEYOR. CONTINUOUS SPECIAL INSPECTION BY THE GEOTECHNICAL ENGINEER DURING EXCAVATION AND SHORING INSTALLATION SHALL BE PROVIDED.

EXCAVATION PLAN

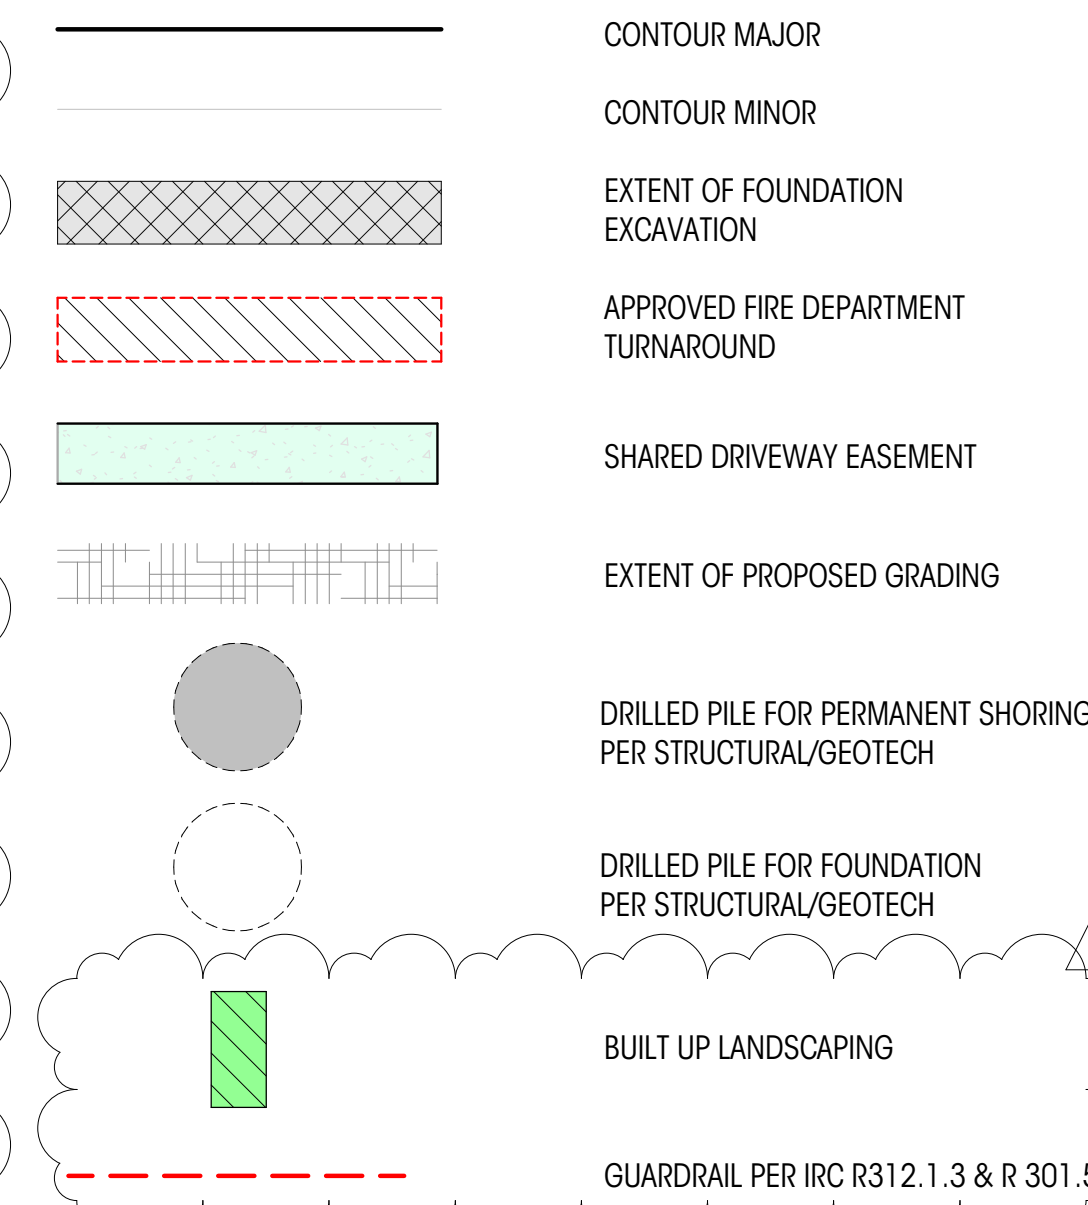

CONSTRUCTION

- REMOVE TREES
- DRILL/INSTALL SHORING PILES FOR STABILIZATION WALL
- EXCAVATE REMAINING SITE
- SCRAPE BUILDING PAD
- FOUNDATION FORMWORK
- FOUNDATION INSTALL
- RETAINING WALL FORMWORK
- DRAIN MAT INSTALL & TRENCHING FOR DRAINAGE AND UTILITIES
- NON-STRUCTURAL RAT-SLAB INSTALL
- FORM PARKING PAD FOUNDATION
- POUR PARKING PAD FOUNDATIONS
- FORM PARKING PAD RETAINING WALLS
- FORM PARKING PAD & GARAGE SLAB
- POUR PARKING/GARAGE SLABS
- FINAL ROUGH GRADING
- FRAMING

NOTE: NO SOIL, WATER, OR DEBRIS FROM SITE ACTIVITIES WILL BE ALLOWED TO BE PLACED OR DISCHARGED ON THE SLOPE.

